


WATERWAY PLAN

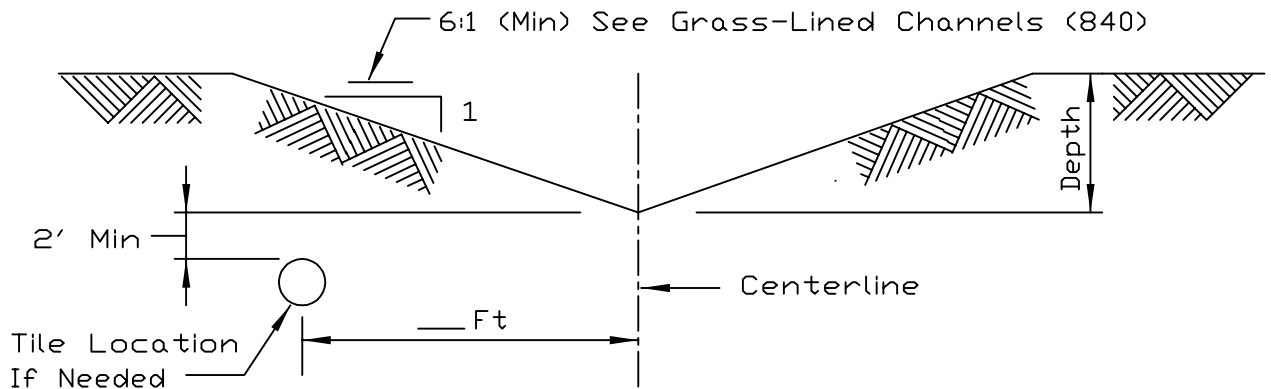

Waterway No.			
From Station			
To Station			
Grade, %			
Drainage Area, Ac.			
Construction Layout Data			
Top Width, Ft.			
Side Slope			
Depth, Ft.			
Tile Diameter, In.			
Tile Length, Ft.			
Grade Check Spacing, Ft.			
Rock ____ Fabric ____			

NOTES:

1. All trees, stumps, brush and debris shall be removed from the construction area and disposed of properly.
2. When required, topsoil shall be salvaged and spread uniformly over disturbed areas.
3. Spoil material from construction will be deposited in low areas or otherwise spread so as not to interfere with flow of water into the waterway. Any earth fill shall be compacted to prevent differential settlement in the completed waterway. The waterway will be constructed to the specified grade, width and depth.
4. Temporary dikes may be constructed around the tops and sides of waterways to divert runoff from new seedlings. Temporary dikes shall be removed as soon as vegetation is established.

REFERENCE
 Project _____
 Designed _____ Date _____
 Checked _____ Date _____
 Approved _____ Date _____



Natural Resources Conservation Service

NRCS

STANDARD DWG. NO.
 IL-540V
 SHEET 1 OF 1
 DATE 6-24-93
